

July 4, 2019

## UPDATE

### Residual Solids Conveyance Line: Esquimalt

Construction of the Residual Solids Conveyance Line has resumed in Esquimalt on the following streets during July and August: Head, Gore, Lyall, and the final section of Wollaston. This work is happening while the summer truck route is in effect (see map on reverse). There is also pipe installation on Anson Street and Bewdley Avenue for the Macaulay Forcemain.

Construction is progressing well with over 40% of the pipes installed. There are multiple crews working along the 19km alignment with pipes also currently being installed in Saanich on Grange Road, Interurban Road, and the Interurban Rail Trail. A regularly updated progress map can be found at [wastewaterproject.ca](http://wastewaterproject.ca).

#### What to Expect

- The pipe will be installed in segments.
- A trench will be excavated, the pipes will be installed and the trench will be backfilled. The surface will be temporarily restored at the end of each work day.
- Final restoration will take place after each section has been tested and completed.
- Rock encountered in the trench will be removed by blasting or mechanical means.
- Noise associated with this work includes excavation machinery and truck back-up beepers, and will not exceed the municipal noise bylaws.
- Pipes and equipment will be temporarily stored in the area while this work is completed.

#### Work Hours

- Monday to Friday from 7:00 a.m. to 7:00 p.m.
- Occasional Saturday work may be required and hours will fall within municipality bylaws.

#### Traffic Impacts

- There will be single lane alternating traffic in the work zones controlled by flaggers.
- There will be temporary parking impacts when work is being completed. Parking signs will be posted in advance.

#### Access

- Access to residents and businesses will be temporarily impacted when work is underway and will be reinstated at the end of each work day. Residents will be notified of temporary closures in advance.

*Thank you for your patience as this work is completed.*

(See maps on reverse)

---

**Any questions about the work, please contact the Project Team.**



**24/7 Phone Line**  
1.844.815.6132



**Email**  
[wastewater@crd.bc.ca](mailto:wastewater@crd.bc.ca)




**Website**  
[wastewaterproject.ca](http://wastewaterproject.ca)

**Summer Truck Route**



**RSCL Construction Progress Map**

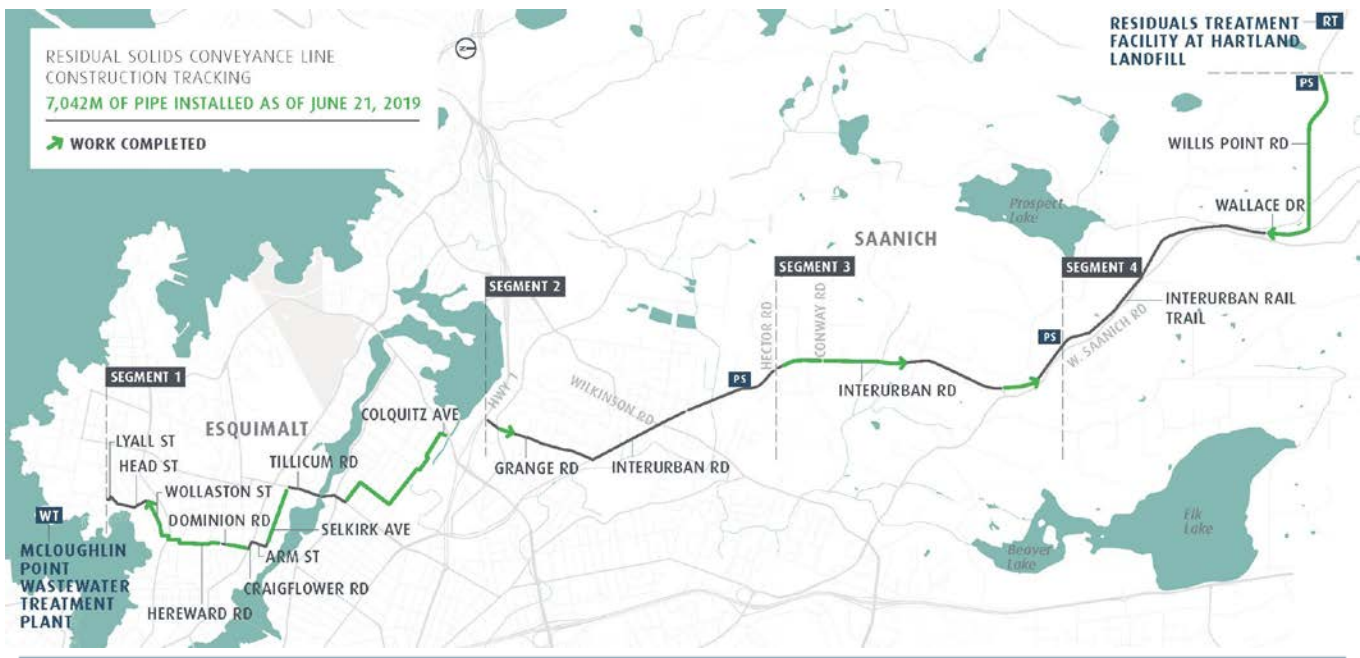

**Any questions about the work, please contact the Project Team.**



**24/7 Phone Line**  
1.844.815.6132



**Email**  
wastewater@crd.bc.ca



**Website**  
wastewaterproject.ca
